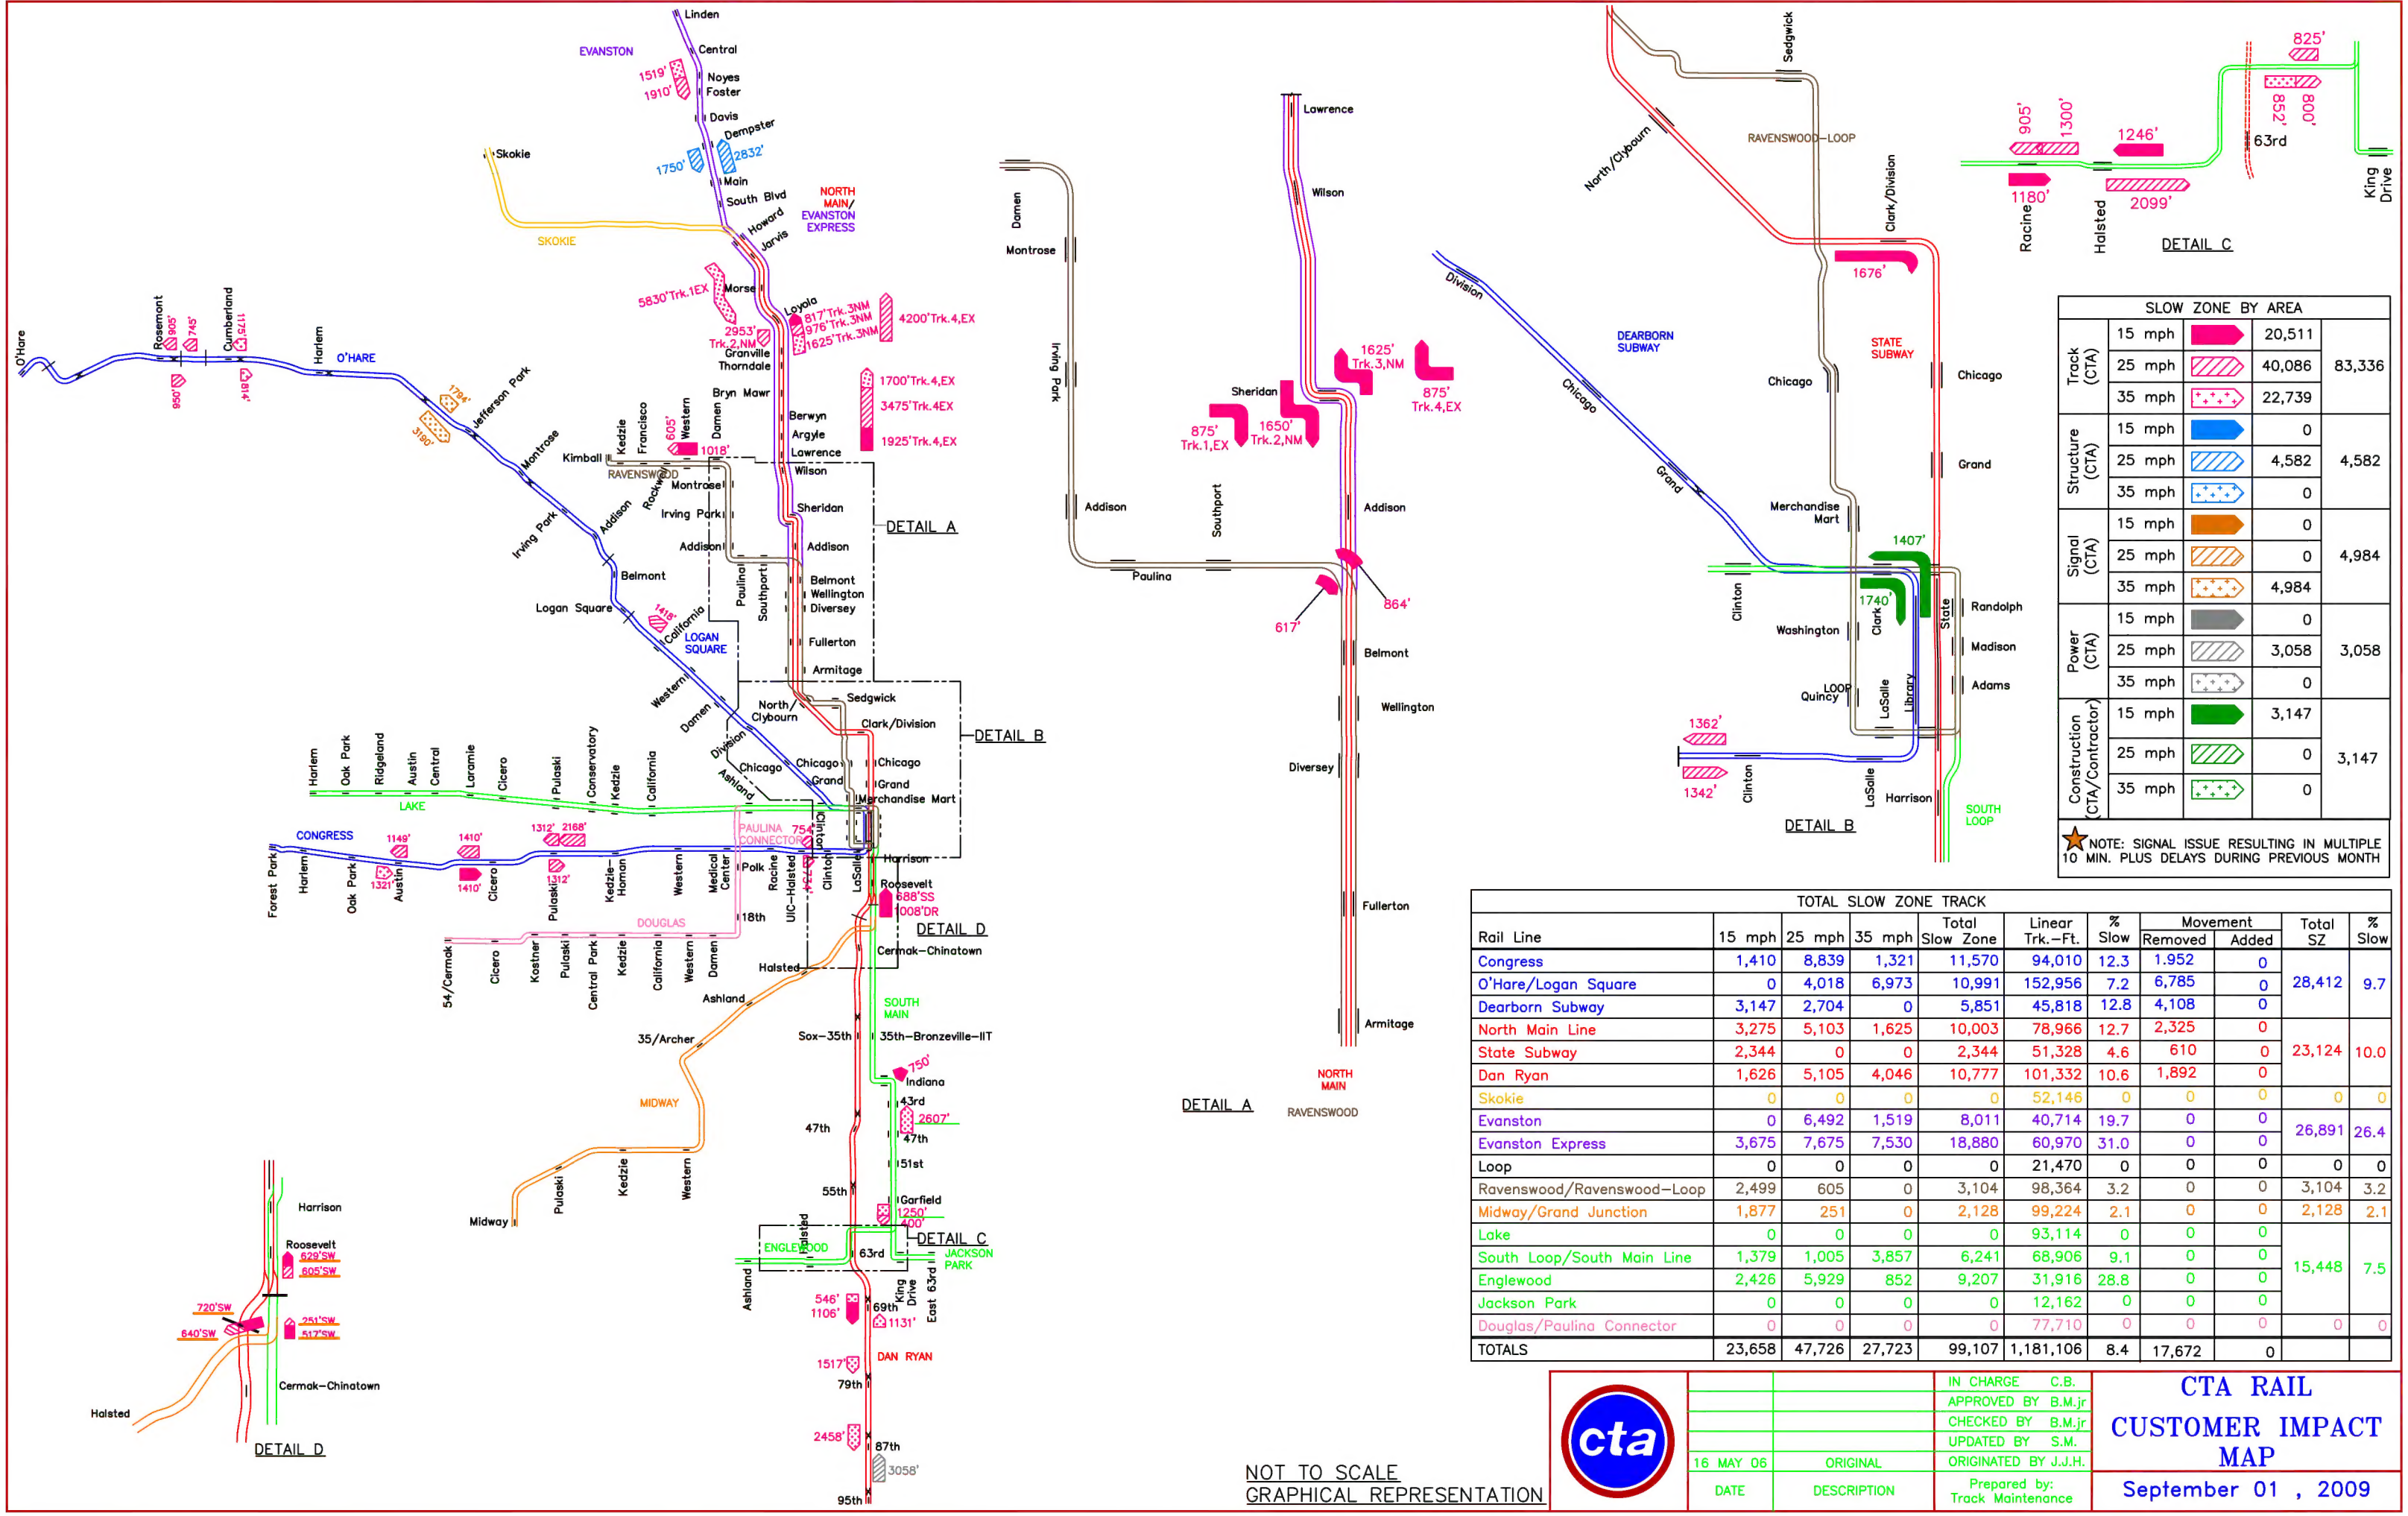

SLOW ZONE BY AREA				
Track (CTA)	15 mph		20,511	83,336
	25 mph		40,086	
	35 mph		22,739	
Structure (CTA)	15 mph		0	4,582
	25 mph		4,582	
	35 mph		0	
Signal (CTA)	15 mph		0	4,984
	25 mph		0	
	35 mph		4,984	
Power (CTA)	15 mph		0	3,058
	25 mph		3,058	
	35 mph		0	
Construction (CTA/Contractor)	15 mph		3,147	3,147
	25 mph		0	
	35 mph		0	

★ NOTE: SIGNAL ISSUE RESULTING IN MULTIPLE 10 MIN. PLUS DELAYS DURING PREVIOUS MONTH

TOTAL SLOW ZONE TRACK										
Rail Line	15 mph	25 mph	35 mph	Total Slow Zone	Linear Trk.–Ft.	% Slow	Movement Removed	Movement Added	Total SZ	% Slow
Congress	1,410	8,839	1,321	11,570	94,010	12.3	1.952	0	28,412	9.7
O'Hare/Logan Square	0	4,018	6,973	10,991	152,956	7.2	6,785	0		
Dearborn Subway	3,147	2,704	0	5,851	45,818	12.8	4,108	0		
North Main Line	3,275	5,103	1,625	10,003	78,966	12.7	2,325	0	23,124	10.0
State Subway	2,344	0	0	2,344	51,328	4.6	610	0		
Dan Ryan	1,626	5,105	4,046	10,777	101,332	10.6	1,892	0		
Skokie	0	0	0	0	52,146	0	0	0	0	0
Evanston	0	6,492	1,519	8,011	40,714	19.7	0	0	26,891	26.4
Evanston Express	3,675	7,675	7,530	18,880	60,970	31.0	0	0		
Loop	0	0	0	0	21,470	0	0	0	0	0
Ravenswood/Ravenswood–Loop	2,499	605	0	3,104	98,364	3.2	0	0	3,104	3.2
Midway/Grand Junction	1,877	251	0	2,128	99,224	2.1	0	0	2,128	2.1
Lake	0	0	0	0	93,114	0	0	0	15,448	7.5
South Loop/South Main Line	1,379	1,005	3,857	6,241	68,906	9.1	0	0		
Englewood	2,426	5,929	852	9,207	31,916	28.8	0	0		
Jackson Park	0	0	0	0	12,162	0	0	0		
Douglas/Paulina Connector	0	0	0	0	77,710	0	0	0	0	0
TOTALS	23,658	47,726	27,723	99,107	1,181,106	8.4	17,672	0		

NOT TO SCALE
GRAPHICAL REPRESENTATION

DATE	DESCRIPTION	
		IN CHARGE C.B.
		APPROVED BY B.M.jr
		CHECKED BY B.M.jr
		UPDATED BY S.M.
16 MAY 06	ORIGINAL	ORIGINATED BY J.J.H.
		Prepared by: Track Maintenance

CTA RAIL
CUSTOMER IMPACT MAP
September 01 , 2009
